AREA 3 MINNESOTA RIVERBANK STABILIZATION

ID	Task Name	Duration	Start	Finish
1	**Area 3 Minnesota Riverbank**	**74 days**	**Thu 11/20/25**	**Tue 3/3/26**
2	Mobilization	0 days	Thu 11/20/25	Thu 11/20/25
3	Clearing & Grubbing	2 days	Thu 11/20/25	Fri 11/21/25
4	Preconstruction Survey	5 days	Thu 11/20/25	Wed 11/26/25
5	Erosion Control	3 days	Thu 11/20/25	Mon 11/24/25
6	Site Prep/Staging Access	5 days	Tue 11/25/25	Mon 12/1/25
7	Excavation ~5+00-8+62	8 days	Tue 12/2/25	Thu 12/11/25
8	Riprap ~5+00-8+62	8 days	Fri 12/12/25	Tue 12/23/25
9	Stormsewer Outlet	3 days	Wed 12/24/25	Fri 12/26/25
10	Floodplain Trench	2 days	Mon 12/29/25	Tue 12/30/25
11	Sheetpile Wall 0+00-5+00	15 days	Wed 12/10/25	Tue 12/30/25
12	Excavation 0+00-5+00	11 days	Wed 12/31/25	Wed 1/14/26
13	Riprap 0+00-5+00	12 days	Thu 1/15/26	Fri 1/30/26
14	Toewood	7 days	Mon 2/2/26	Tue 2/10/26
15	Remove Sheetpile Wall	5 days	Mon 2/2/26	Fri 2/6/26
16	Chinking Stone	7 days	Wed 2/11/26	Thu 2/19/26
17	Launchable Toe Cover/Fill	7 days	Fri 2/20/26	Mon 3/2/26
18	Restoration	5 days	Wed 2/25/26	Tue 3/3/26

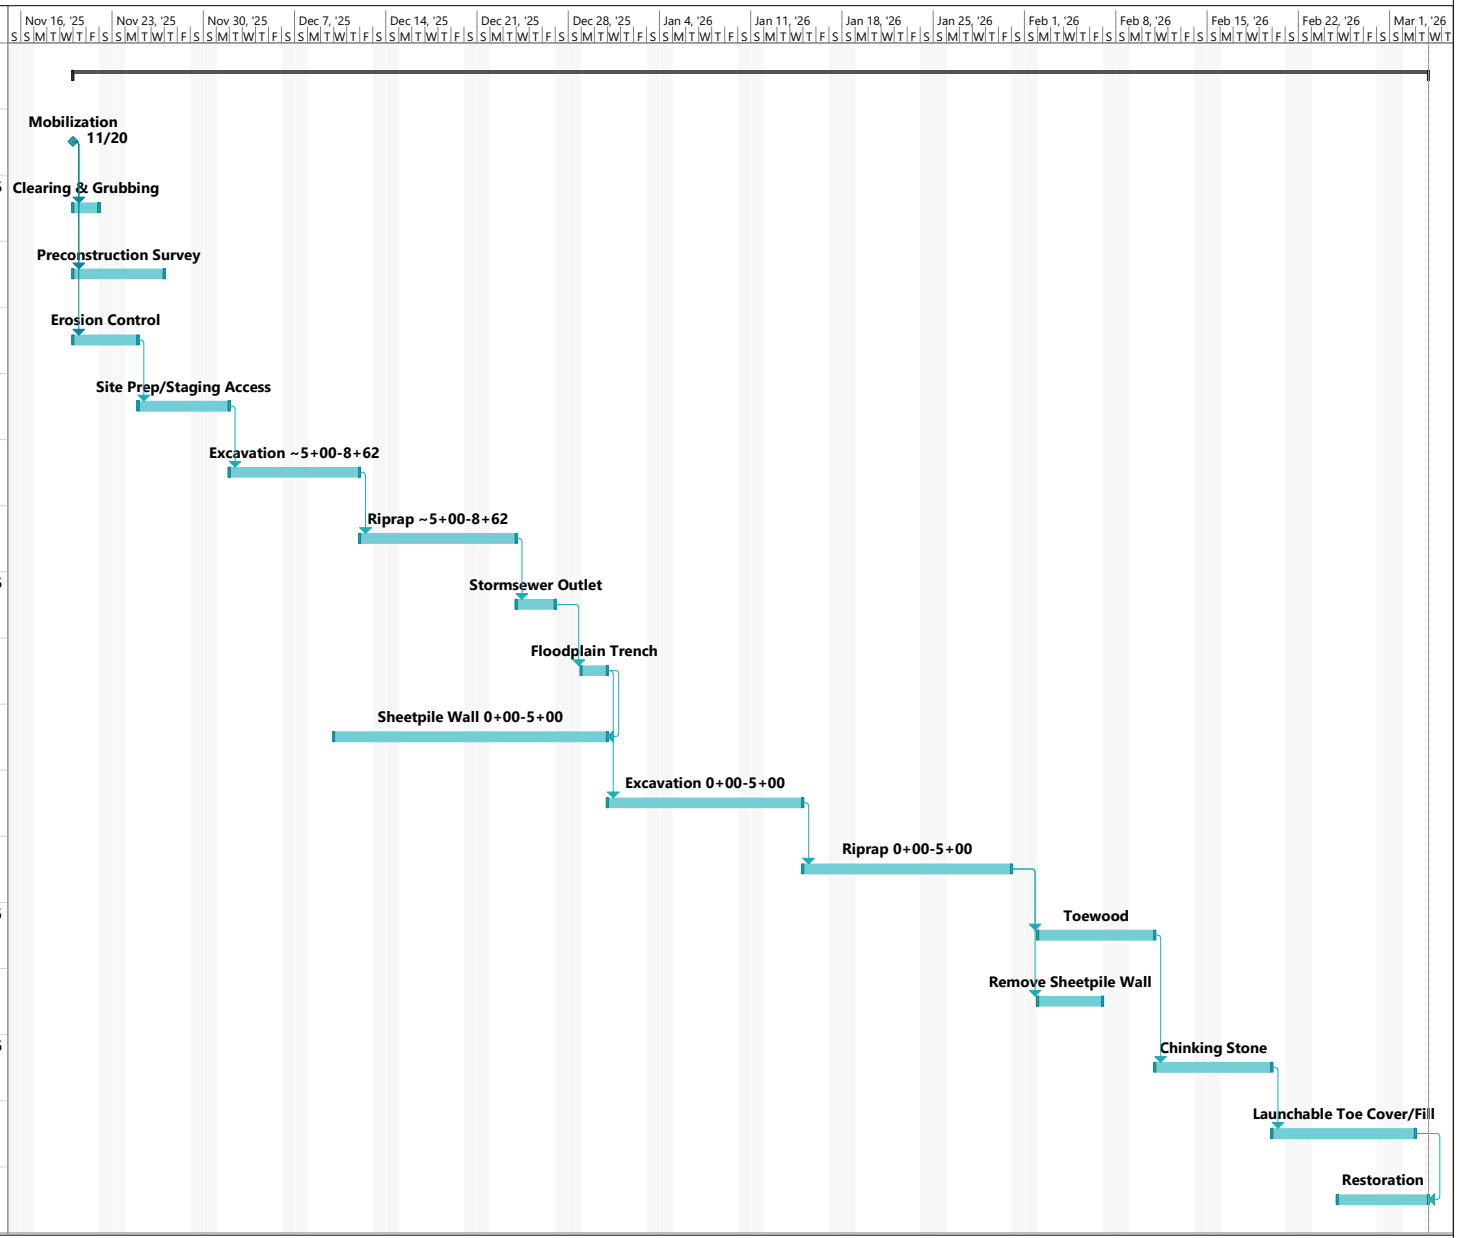

Project: Area 3 Riverbank
Date: Tue 11/11/25

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
